

Brighton Guardrail Inspection Report City of Brighton, CO			
Date of Inspection and location:			
Structure ID:	5		
Date of Inspection:	06/14/2019		
Inspector:	Gerardo Martinez		
Location:	E. Crown Prince Blvd		
Nearest Intersection:	Main St (CR27)		
X-coordinate			
Y-coordinate			
Inventory Data:			
Guardrail Photos:	Attached	Shoulder Condition:	Good
Guardrail Condition:	N/A	Number of Total Post:	N/A
Length of Guardrail (ft.):	N/A	Number of Bad Post:	N/A
Height of Guardrail (in.):	N/A	Number of Missing or loose hardware components:	None
Direction of Travel:	Westbound (WB)	Rating of Damage:	N/A
End Terminal type:	N/A	Priority for Repair: (1-5, 1 being highest need for repair)	1
Guardrail Section(s) Missing:	N/A		
Comments:			
No guardrail is in place; slab is about 22 feet. Priority 1			

No Guardrail Photo:




FIGURE 13: VIEWING NORTH ON THE WESTBOUND SIDE OF THE DITCH

Brighton Guardrail Inspection Report City of Brighton, CO			
Date of Inspection and location:			
Structure ID:	11		
Date of Inspection:	06/21/2019		
Inspector:	Gerardo Martinez		
Location:	Baseline Road (CR2)		
Nearest Intersection:	Main St (CR27)		
X-coordinate			
Y-coordinate			
Inventory Data:			
Guardrail Photos:	Attached	Shoulder Condition:	Good
Guardrail Condition:	Good	Number of Total Post:	2
Length of Guardrail (ft.):	15	Number of Bad Post:	None
Height of Guardrail (in.):	29	Number of Missing or loose hardware components:	None
Direction of Travel:	Westbound (WB)	Rating of Damage:	Moderate
End Terminal type:	Fish End Terminal	Priority for Repair: (1-5, 1 being highest need for repair)	5
Guardrail Section(s) Missing:	N/A		
Comments:			
Minor westbound damage but guardrail remains operational. Priority 5			

No Guardrail Photos:




FIGURE 22: VIEWING GUARDRAIL FROM THE EAST IN THE WESTBOUND DIRECTION APPROACHING MAIN STREET (CR27)



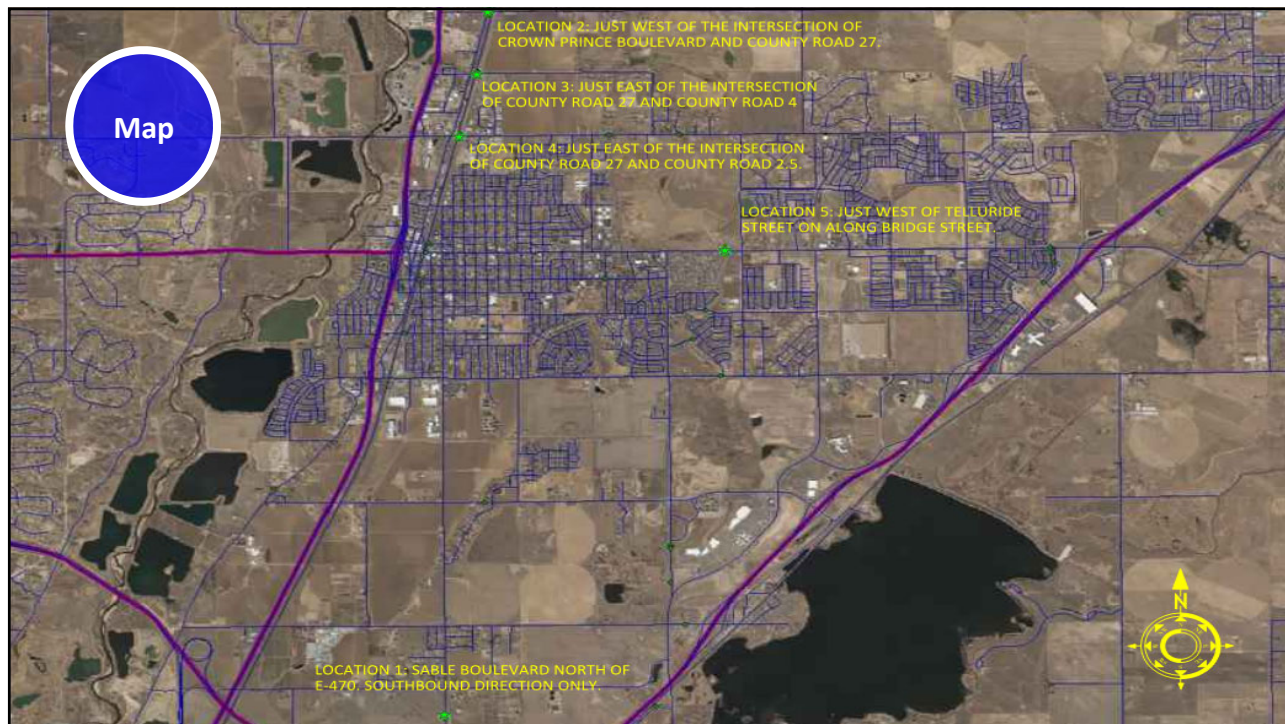


FIGURE 23: MINOR BEND TO GUARDRAIL IN THE WESTBOUND SIDE








BIDDER	AMOUNT	SCORE	Financials
Adarand Constructors, Inc.	\$221,147.00	91.6	
Cruz Construction, Inc.	\$113,490.00	93.3	

ITEM	AMOUNT	Financials
Budget	\$165,000.00	
Engineer Estimate	\$157,000.00	
Contract Award	\$113,490.00	

Schedule	
TASK	DATE
Award Project	October 30, 2019
Initial Construction	December 1, 2019
Completion of Construction*	April 30, 2020



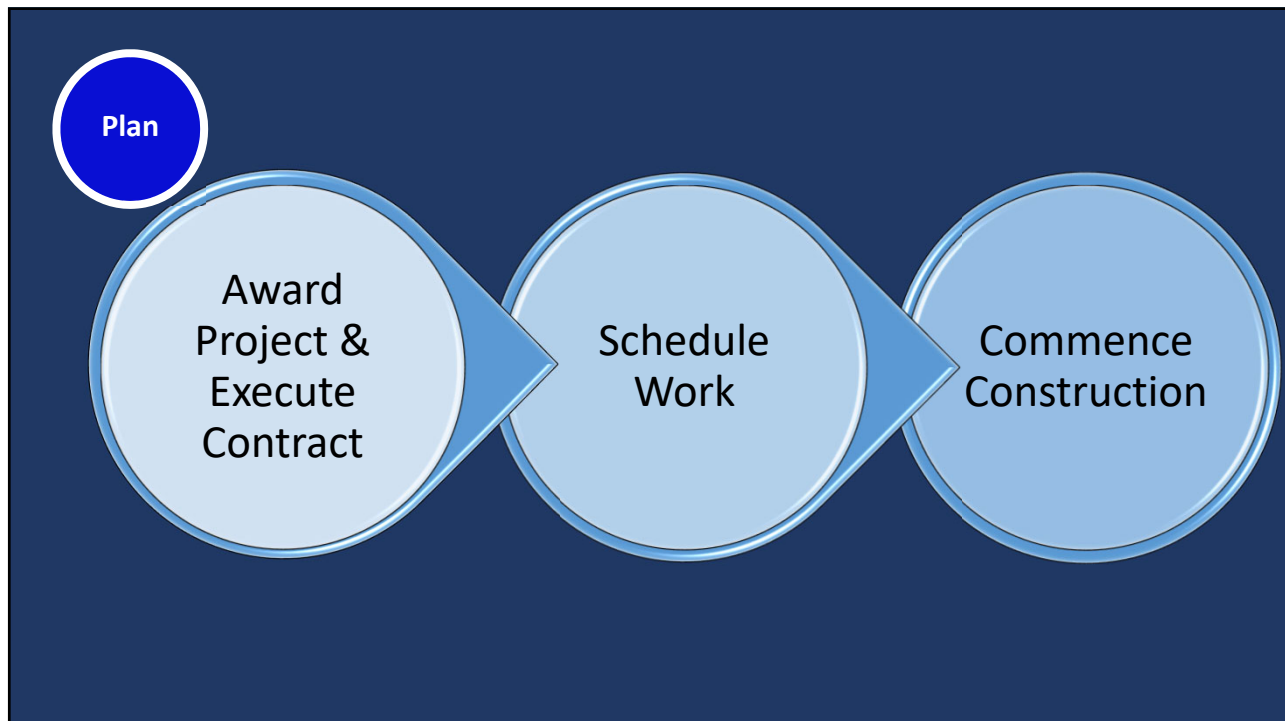



2019 Street Preservation
Change Order
Public Works Department
